

Late and over budget.

What drives schedule slips and budget growth across New York City's \$160B capital portfolio, May 2023 to May 2026.

Source: NYC Open Data, Capital Projects Dashboard
10 reporting snapshots · 132,484 raw rows
Python · MySQL · Analysis by Shivam Singh

Portfolio budget

\$160.3B

Deduplicated, May 2026 snapshot

Budget growth

+10.2%

\$145.5B → \$160.3B since May 2023

Projects tracked

2,812

With forecast completion dates

Projects that slipped

55.2%

Forecast completion moved later

Average slip

282 days

About 9 months per project



DATA QUALITY

A \$47B double count, caught before analysis

One budget line can fund several projects, and the raw table repeats its full amount on every linked project. The correct grain is one row per snapshot, FMS ID and agency.

Naïve sum of all rows

\$207.59B

+ \$47.25B · overstated by 29%

One row per FMS ID



\$159.71B

− \$0.63B · drops agency splits

One row per FMS ID + agency

\$160.34B


Correct grain · verified in Python and SQL

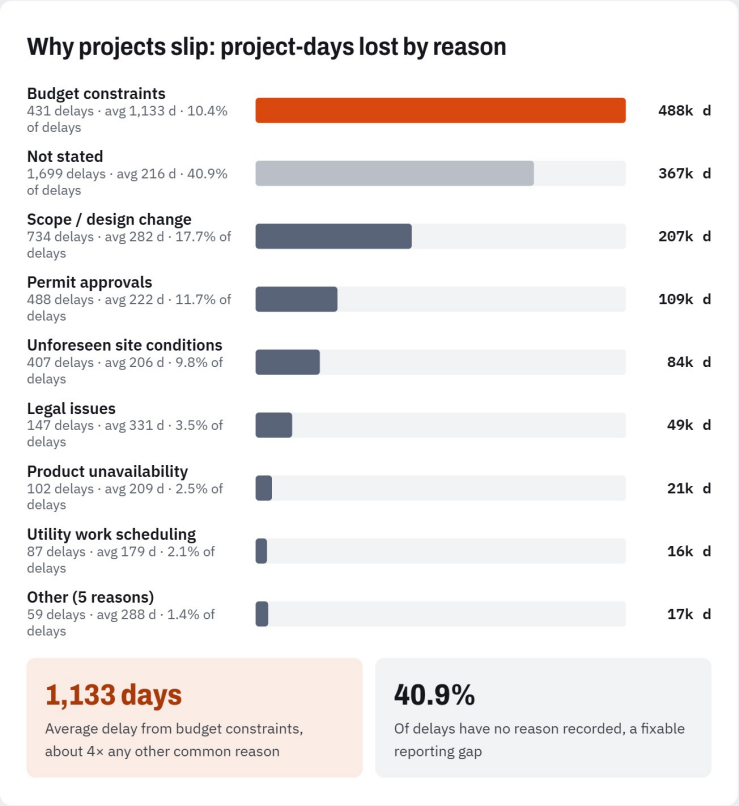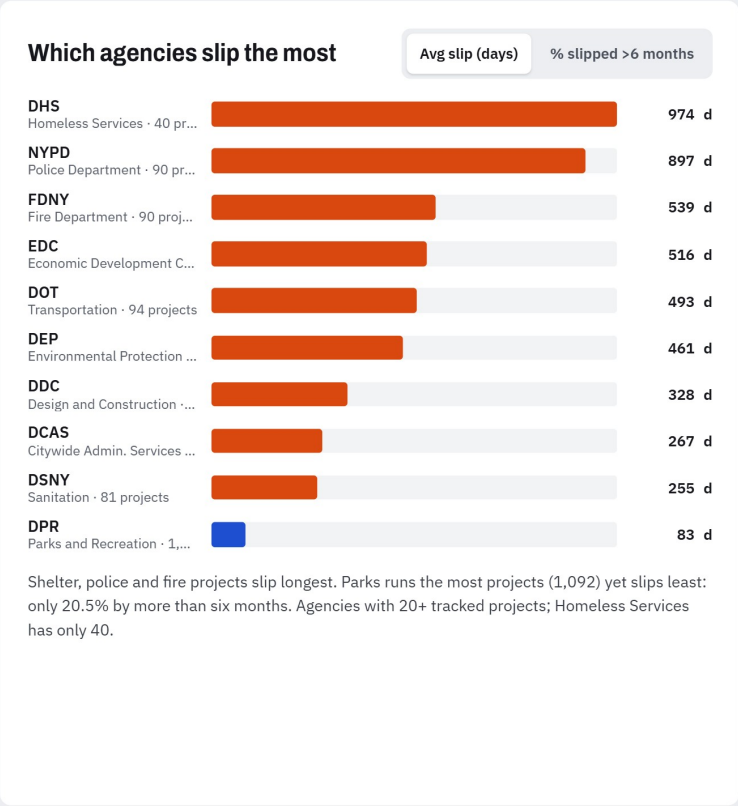

Budget change by agency, May 2023 → May 2026

\$M · largest increases and decreases

Bigger projects slip more

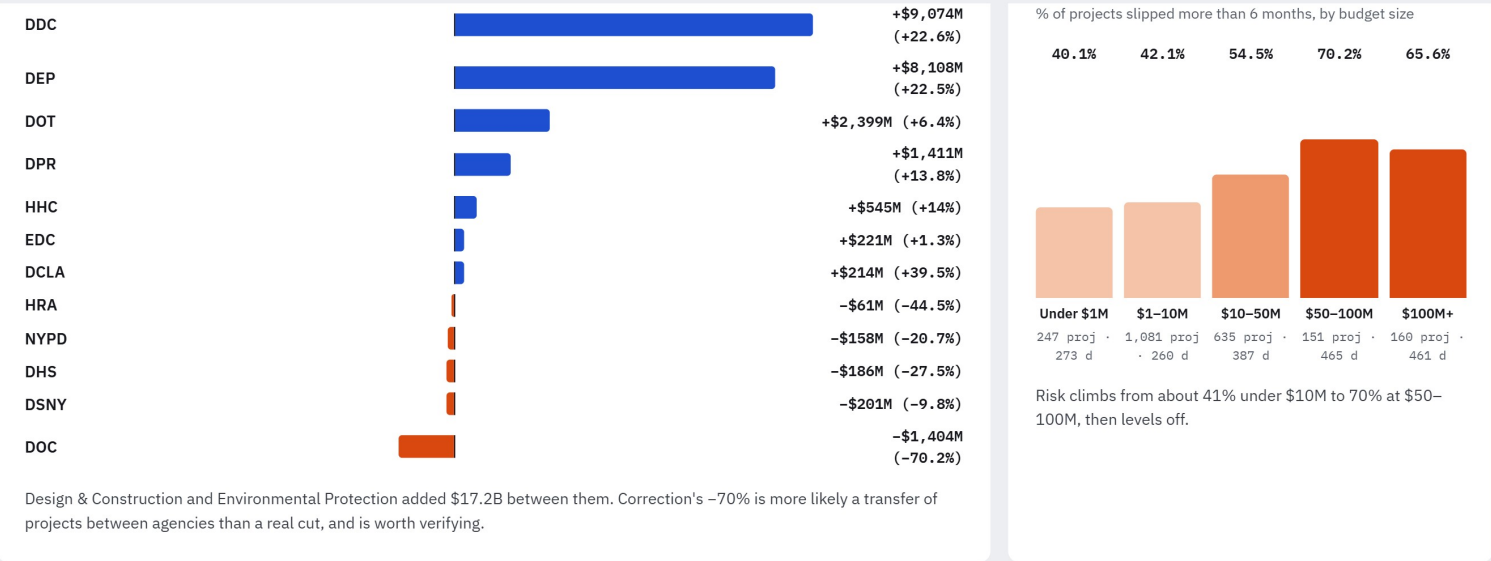

At-risk watchlist

Active projects with 3+ reported delays or a slip of over a year, longest slip first

- All (25)
- Design (16)
- Procurement (4)
- Construction (5)

PROJECT	AGENCY	BOROUGH	PHASE	DELAYS	SLIP	FORECAST	BUDGET
BRX2110 Boston Road Bridge over Bronx River Extreme value: check forecast history	DOT	Bronx	Design	3	12.3 yrs	11/10/2040	\$21.9M
St. George Ferry Terminal Waterfront Remediation	DOT	Staten Island	Design	3	10.6 yrs	12/31/2036	\$19.1M
Hunts Point Meat Market Capital Improvements	EDC	Bronx	Construction	2	7.9 yrs	05/30/2033	\$113.3M
HPFFM Fire Alarm Modifications & Trench Drain Replacement	EDC	Bronx	Construction	2	7.9 yrs	11/20/2032	\$27.2M
Emergency Reconstruction of 1 Police Plaza Facade	NYPD	Manhattan	Design	4	7.5 yrs	12/30/2031	\$18.7M
DEL-194 Reconstruction of Merriman Dam Spillway	DEP	Citywide	Procurement	8	7.3 yrs	08/31/2033	\$45.0M
32nd Precinct Parking Lot	NYPD	Manhattan	Design	2	7.0 yrs	01/15/2033	\$0.1M
HBQA23176 BCIP over Dutch Broadway	DOT	Queens	Design	4	6.8 yrs	02/26/2036	\$42.8M
Valve Replacements at East Delaware Release Chamber	DEP	Citywide	Procurement	3	6.4 yrs	09/15/2031	\$22.5M
HBM1221 E 25th Street Pedestrian Bridge over FDR	DOT	Manhattan	Design	3	5.9 yrs	07/28/2035	\$0.9M
KEC-7 Wetland Mitigation	DEP	Citywide	Procurement	5	5.9 yrs	08/12/2031	\$530.5M
600 FCD Facade and Paving	EDC	Bronx	Construction	4	5.3 yrs	12/31/2029	\$4.5M
ADA	NYPD	Manhattan	Design	6	5.1 yrs	10/16/2029	\$4.2M
DCLA Percent for Art: Monuments	EDC	Manhattan	Design	3	5.1 yrs	12/31/2028	\$2.0M
Raise Shorelines Citywide Exactly 5 years: possible placeholder date	EDC	Staten Island	Construction	2	5.0 yrs	12/31/2031	\$107.9M
Queens 8/10/12 Garage Rehab Exactly 5 years: possible placeholder date	DSNY	Queens	Design	1	5.0 yrs	09/30/2034	\$29.5M
Manhattan 128 West 17 St Rehab (PID 4579) Exactly 5 years: possible placeholder date	DSNY	Manhattan	Design	2	5.0 yrs	06/30/2034	\$11.4M
Manhattan 128 West 17 St Rehab (PID 4665) Exactly 5 years: possible placeholder date	DSNY	Manhattan	Design	2	5.0 yrs	06/30/2034	\$0.1M
PS-290 Connor Street Pumping Station	DEP	Bronx	Design	5	5.0 yrs	05/19/2031	\$121.2M
Digester Rehabilitation	DEP	Manhattan	Construction	2	5.0 yrs	12/30/2028	\$26.4M
23rd Street Warehouse Reconstruction	NYPD	Brooklyn	Design	2	4.9 yrs	02/18/2032	\$15.6M

CAT-431 Reconstruction of the Lower Catskill Aqueduct	DEP	Citywide	Design	2		4.9 yrs	07/04/2034	\$309.3M
Harbor Charlie Floating Docks Renovation	NYPD	Brooklyn	Design	6		4.9 yrs	12/31/2029	\$4.2M
Jamaica Family Exterior Facade Reconstruction	DHS	Queens	Design	3		4.9 yrs	06/30/2030	\$3.2M
24th Precinct Facade	NYPD	Manhattan	Procurement	5		4.7 yrs	10/31/2029	\$5.3M

How it was built

01 · PYTHON

Profiled three datasets, parsed dates, collapsed 60 phase labels into 8 groups, categorised delay reasons.

02 · GRAIN TEST

Proved budgets are unique per snapshot, FMS ID and agency (100% consistent).

03 · MYSQL

Star schema with a bridge table for the budget-to-project many-to-many; views with window functions.

Caveats

- Budget growth may reflect overruns or planned scope additions; the data does not distinguish them.
- "Original" budgets and forecasts are the earliest in the data (May 2023), not values at approval.
- Several projects slipped exactly 1,826 days (5 years), suggesting placeholder dates. Flagged in the watchlist.
- 26 of 26,598 project snapshots (0.1%) had conflicting forecast dates across funding lines.
